teamgantt
Created with Free Edition

Wastewater Irradiation Exp...	**0h**	**67%**
Cryogenics	**0h**	**97%**
U-Tube Ops for Booster Cool-down	0	0%
UITF Operations	**0h**	**75%**
Booster Charaterization	0	75%
Start HCO	0	0%
Hot Checkout	0	0%
Wastewater (Commissioning)	0	0%
Wastewater Experiment	0	0%
Experiment Complete	0	0%
Chopper slit characterization (op...	**0h**	**93%**
Map encoder to slit	0	0%
CIS/EGG	**0h**	**95%**
Prepare pucks	0	85%
100 mW laser power (install preamp)	0	0%
Installation	**0h**	**74%**
Unistrut Mounting for Cord Hangers	0	0%
Mount Gas Bottle Racks	0	0%
EES-DC	**0h**	**44%**
EES-DC Work	0	17%
Begin Solenoid (MPCM602) Install	**0h**	**70%**
Plumb in Magnet	0	0%
Interface Tests, interlocks, & scalin...	0	60%
Cable Pull (Electricians/2.5 days)	0	75%
Install + checkout w/ EPICS	0	0%
Haimson Corrector Installation	**0h**	**88%**
Haimson Corrector Installation	0	90%
Repurpose Trim Channels	0	80%
Update UED	0	80%
De-installation (1 Week)	0	0%
EES-IC	**0h**	**71%**
BPM installation	**0h**	**99%**
Ready for HCO	0	0%
BCM	**0h**	**39%**
Interface to MPS	0	0%
Current clamping capability	0	0%
Ready for HCO	0	0%
Cameras/Viewers	**0h**	**57%**
Viewers channel reassignments	0	0%
Camera ITVM905+ ARM install - M...	0	90%
Troubleshoot existing viewer issues	0	0%
Ready for HCO	0	0%
Viewer Installation	**0h**	**47%**
Install Viewer #1: ITVM603	**0h**	**43%**
Move electronics etc	0	0%
Install Viewer #2: ITVM604	**0h**	**43%**
Move electronics etc.	0	0%
Faraday Cups/Dumps	**0h**	**96%**
Support FC3 motion onto adjac...	**0h**	**89%**
Cable and Test	0	75%
Build Supports	0	95%
Stack Lead	0	40%
Support FC4 move to M604 cro...	**0h**	**98%**
Cable and test	0	75%
Harp Installation	**0h**	**0%**
IHAM703 TS	**0h**	**0%**
Signal inject IHAM703	0	0%
Break Vacuum?	0	0%
Vacuum	**0h**	**70%**
VFVM401 install	**0h**	**80%**
Electronics Installation	0	65%
Fast Valve Testing	0	0%
VCGM604 install	**0h**	**77%**

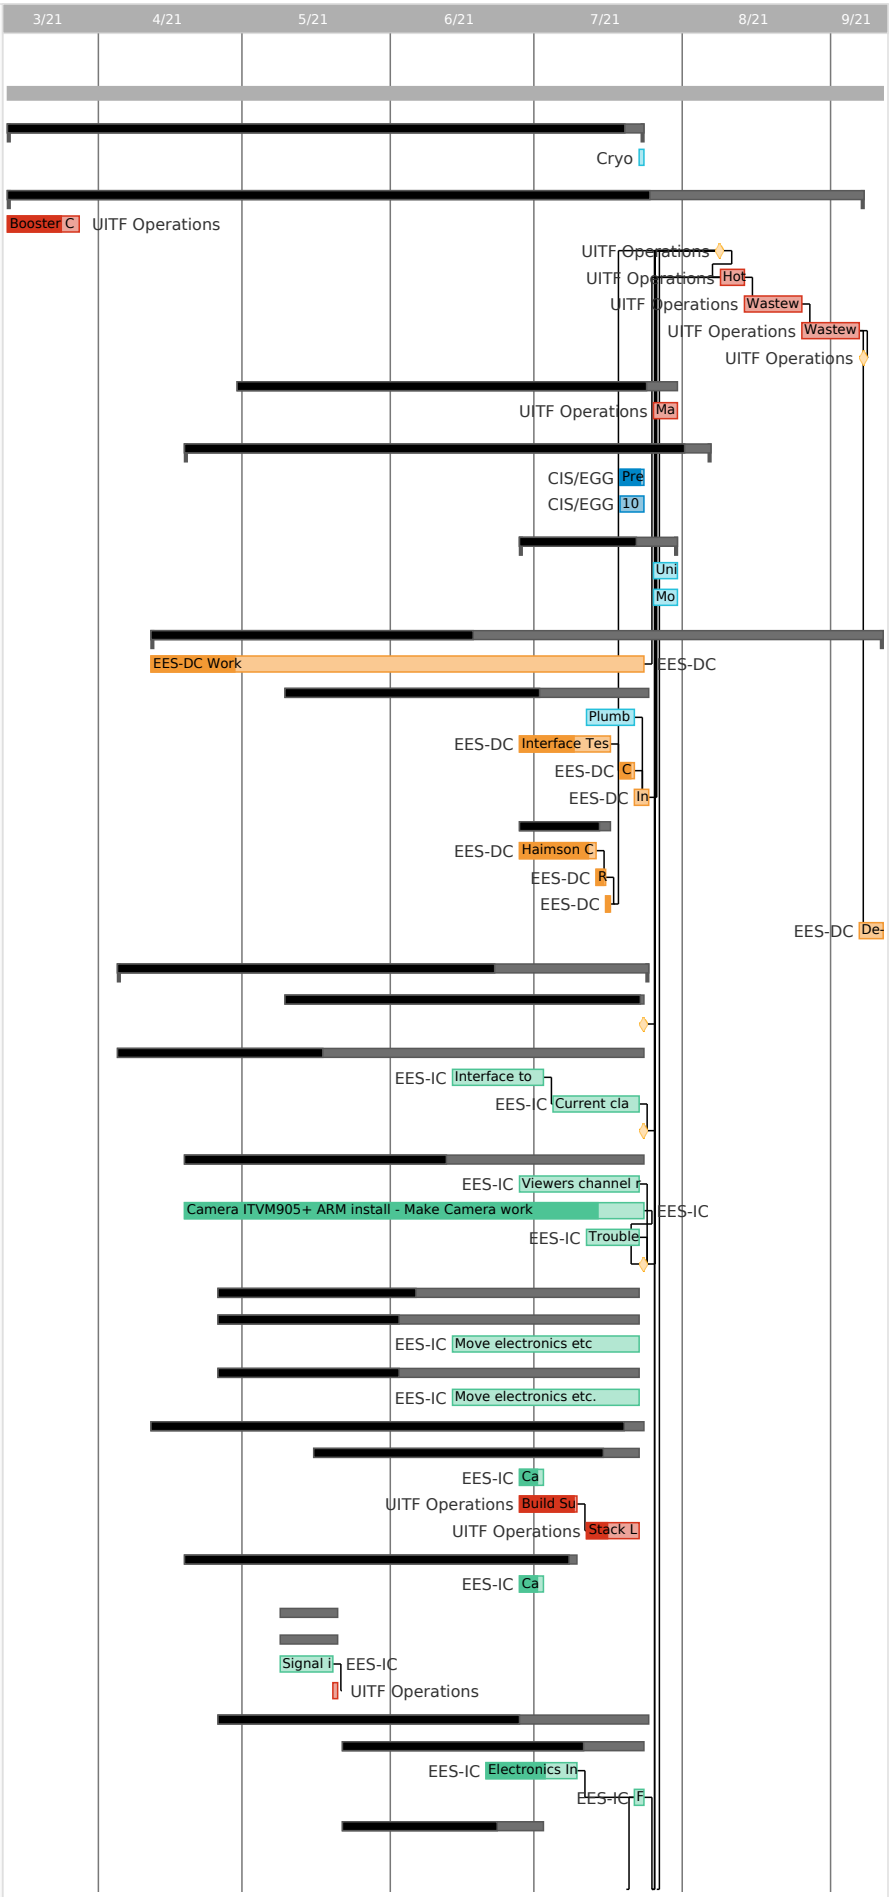

teamgantt
Created with Free Edition
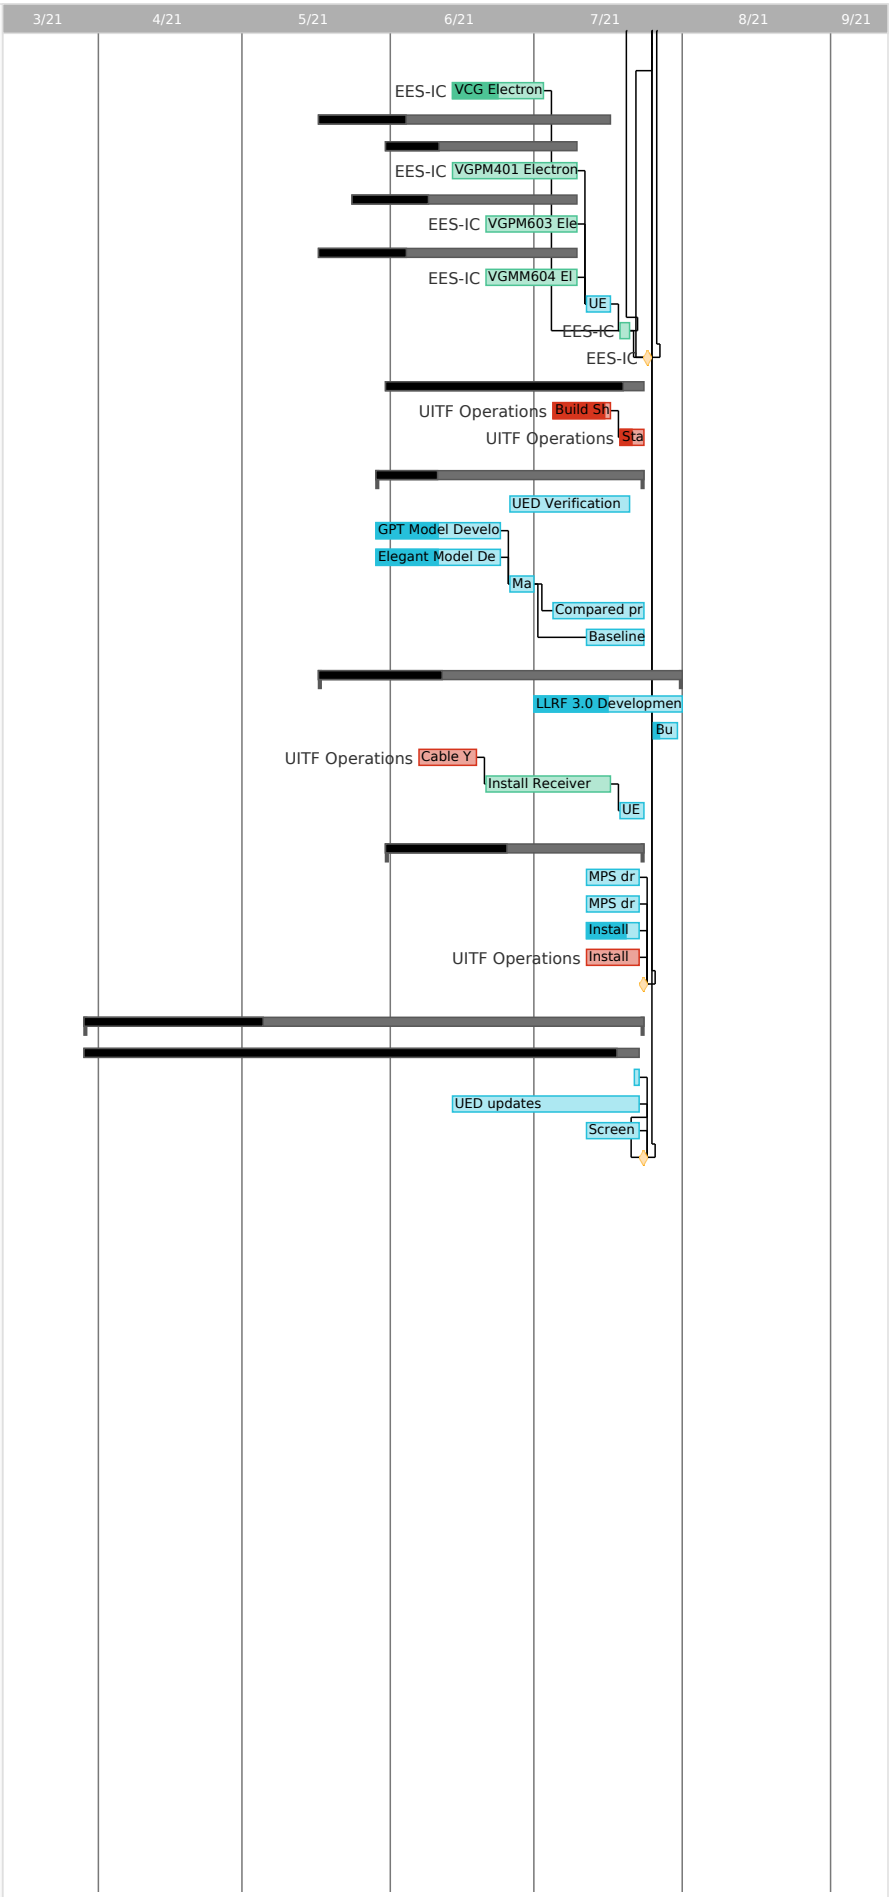
VCG Electronics install	0	50%
NEG Installation	**0h**	**30%**
VGPM401 NEG install	**0h**	**28%**
VGPM401 Electronics/PS install	0	0%
VGPM603 NEG install	**0h**	**34%**
VGPM603 Electronics/PS install	0	0%
VGPM604 NEG install	**0h**	**34%**
VGMM604 Electronics/PS install	0	0%
UED update with NEGs	0	0%
UED updates	0	0%
Vacuum work complete	0	0%
Install Target	**0h**	**92%**
Build Shielding Table	0	90%
Stack shielding blocks	0	50%
CASA/Optics	**0h**	**23%**
UED Verification	0	0%
GPT Model Development	0	50%
Elegant Model Development	0	50%
Machine Twiss Parameter Chart	0	0%
Compared pred. model Espread w/ Al...	0	0%
Baseline Optics Technote	0	0%
LLRF	**0h**	**34%**
LLRF 3.0 Development	0	50%
Buncher Stability Characterization	0	25%
Cable Yao	0	0%
Install Receiver	0	0%
UED: YAO401 > ICV501	0	0%
SSG	**0h**	**47%**
MPS drop #1: Solenoid	0	0%
MPS drop #2: BCM	0	0%
Install BLMs	0	75%
Install Decarad Heads	0	0%
SSG Work Complete	0	0%
Software	**0h**	**32%**
Target Controls	**0h**	**96%**
Test Target Motion Interlock	0	0%
UED updates	0	0%
Screen Updates	0	0%
Software Work Completed	0	0%
