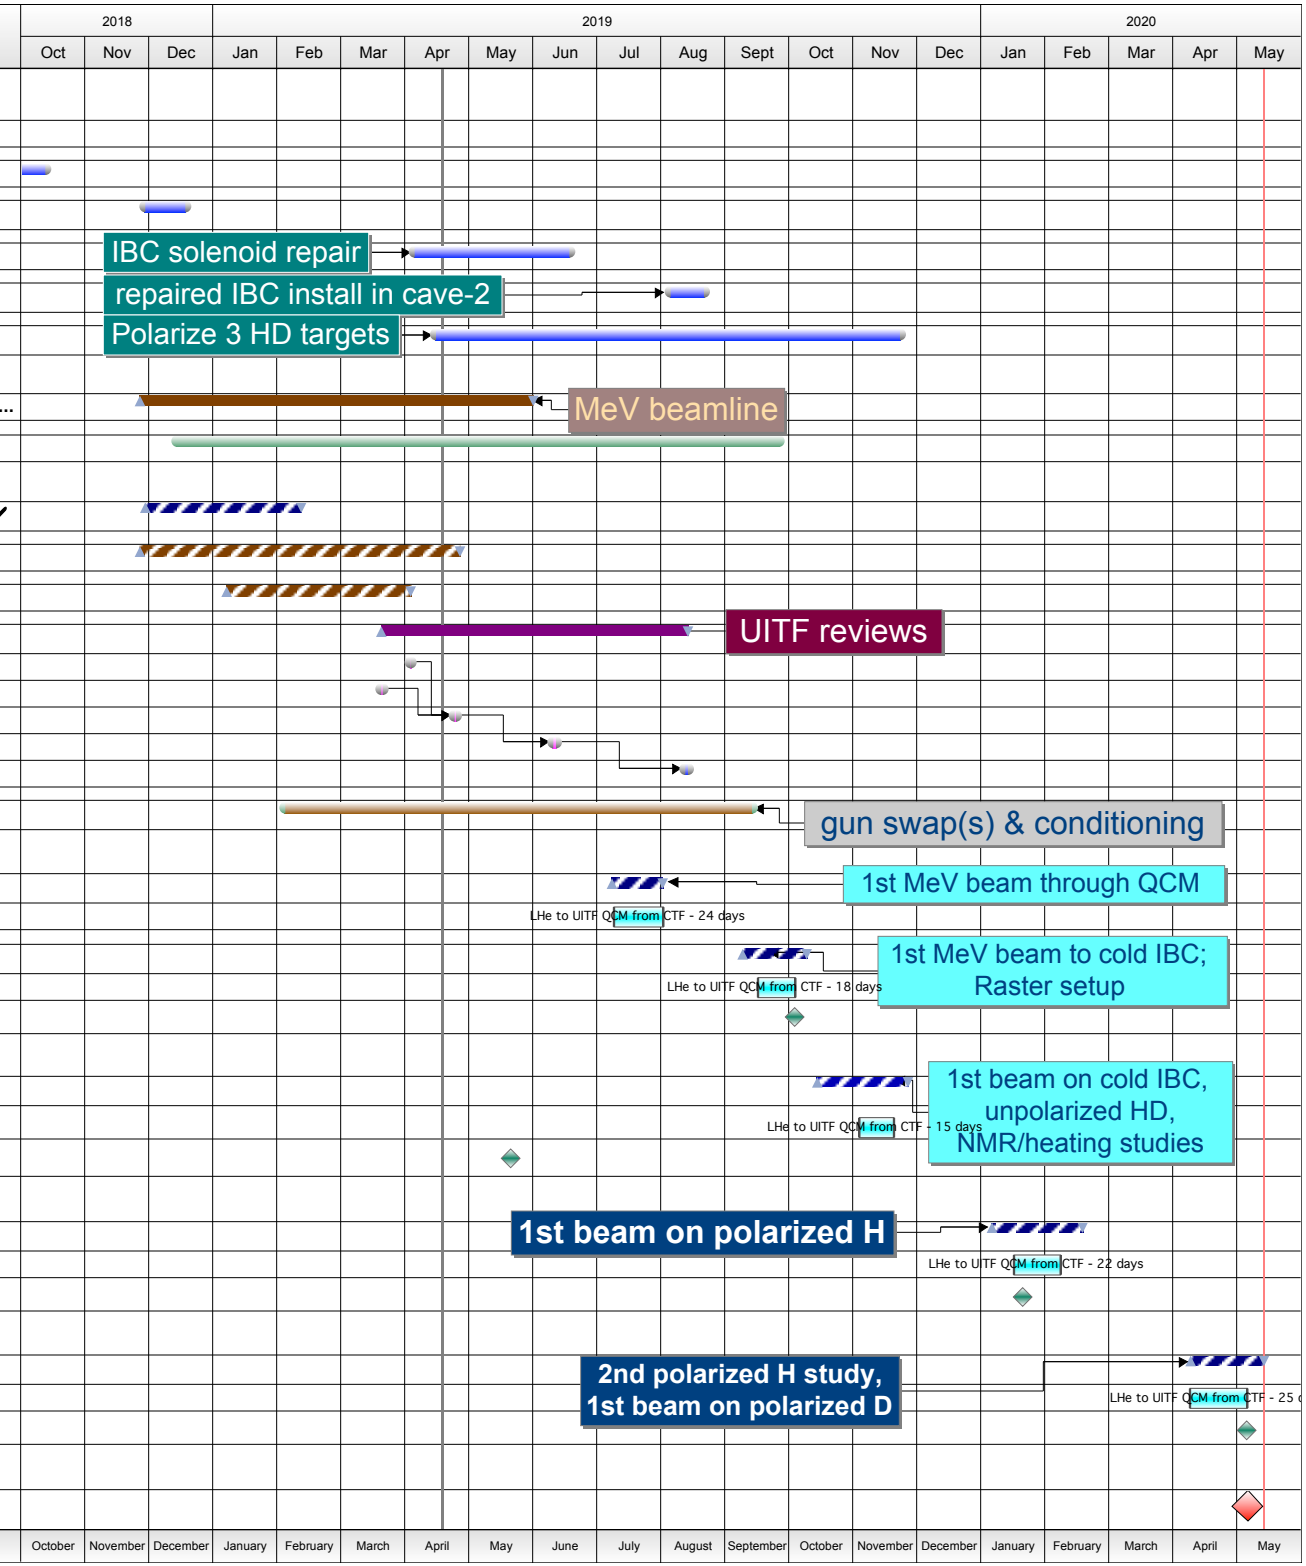	Activity Name	Notes
1	**HDice@UITF schedule**	**Group**
2	(last update: Apr 18/19)	
3		
4	**IBC initial Installation in cave-2...**	**HDice ✔**
12		
13	**IBC cold test at UITF...**	**HDice ✔**
22		
23	**Repair IBC solenoids & reassemble IBC...**	**HDice; SHOPS**
28		
29	**HDice IBC Renstallation in cave-2...**	**HDice**
36		
37	**Polarize 3 HD targets...**	**HDice**
43		
44	**Assemble & instrument cave-2 MeV beamline...**	**Gun,EES,SSG,...**
62		
63	**Halo Counters, Diagnostics & Dump...**	**HDice**
72		
73	**RF power test in 1/4CM...**	**RF,SSG,Cryo ✔**
81		
82	**UITF Shielding...**	**RCG, FM, ...**
86		
87	**PSS BCM (for low current mode)...**	**SSG**
90		
91	**Approvals for low-current UITF OPS**	**...**
92	SCMB evaluation of PSS BCM	
93	UITF Accelerator Operations Directive	
94	Conduct of Operations Review	
95	Accelerator Readiness Review	
96	HDice experimental Readiness review	
97		
98	**UITF gun...**	
109		
110	**1st MeV beam through QCM to waist dump...**	
117	**LHe to UITF QCM from CTF - 24 days**	
118		
119	**1st UITF beam through cold IBC...**	**HDice**
139	**LHe to UITF QCM from CTF - 18 days**	
140	***Milestone: MeV beam through cold IBC***	
141		
142	**1st beam on unpolarized HD...**	**HDice**
162	**LHe to UITF QCM from CTF - 15 days**	
163	***Milestone: 8 MeV beam on unpolarized HD***	
164		
165	**1st e + polarized H test...**	**HDice**
194	**LHe to UITF QCM from CTF - 22 days**	
195	***Milestone: 1st MeV beam on polarized H***	
196		
197	**2nd e + polarized H & D test...**	**HDice**
222	**LHe to UITF QCM from CTF - 25 days**	
223	***Milestone: 1st beam on polarized D***	
224		
225	**QCM removal for installation in CEBAF**
