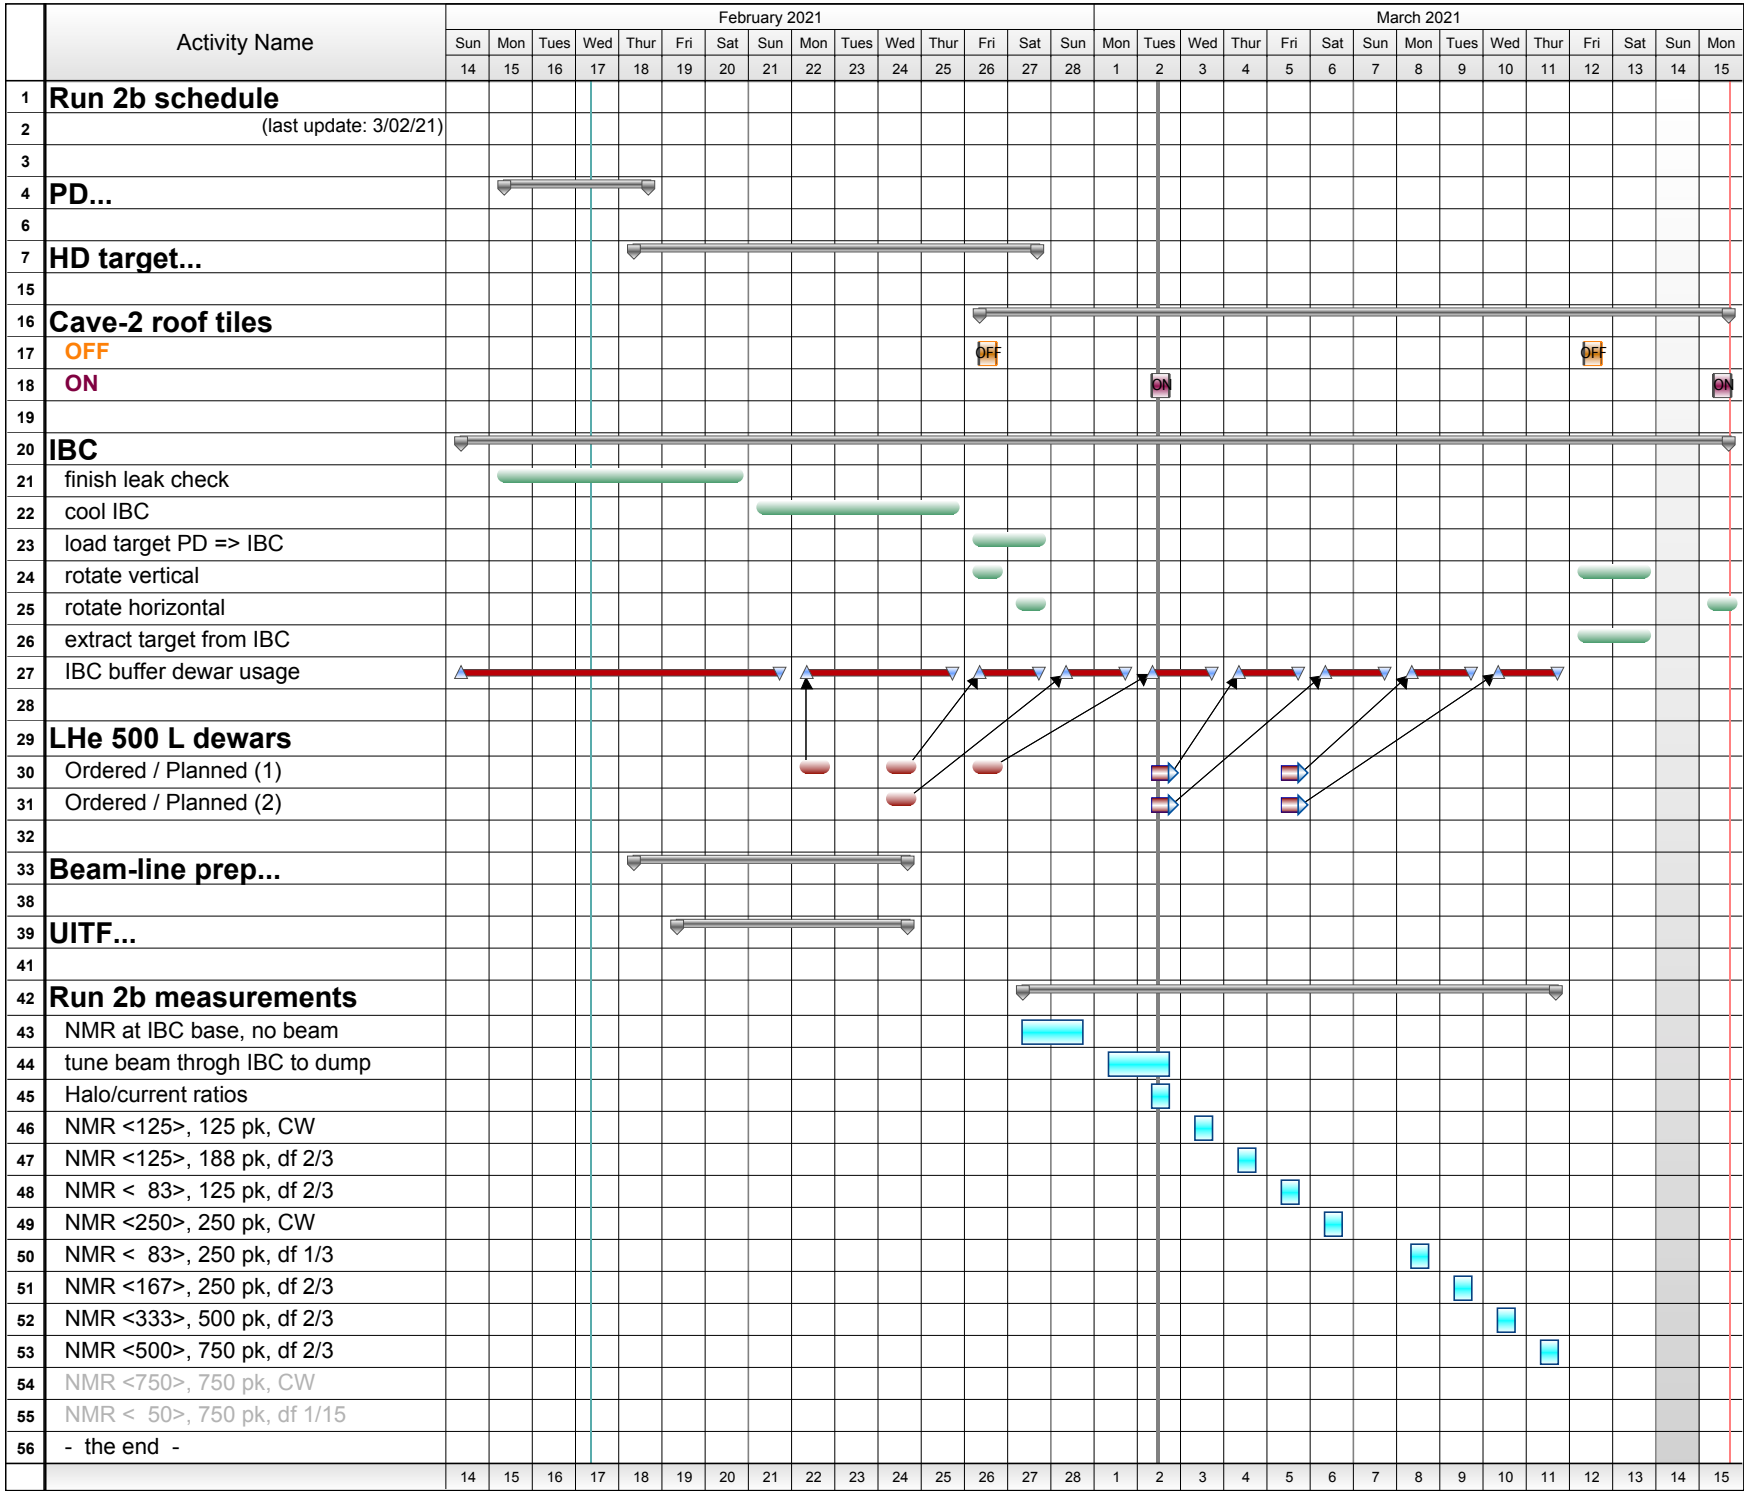
Activity Name
February 2021
March 2021
Sun Mon Tues Wed Thur Fri Sat Sun Mon Tues Wed Thur Fri Sat Sun Mon Tues Wed Thur Fri Sat Sun Mon Tues Wed Thur Fri Sat Sun Mon
14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15
1 Run 2b schedule
2 (last update: 3/02/21)
3
4 PD...
6
7 HD target...
15
16 Cave-2 roof tiles
17 OFF
18 ON
19
20 IBC
21 finish leak check
22 cool IBC
23 load target PD => IBC
24 rotate vertical
25 rotate horizontal
26 extract target from IBC
27 IBC buffer dewar usage
28
29 LHe 500 L dewars
30 Ordered / Planned (1)
31 Ordered / Planned (2)
32
33 Beam-line prep...
38
39 UITF...
41
42 Run 2b measurements
43 NMR at IBC base, no beam
44 tune beam throgh IBC to dump
45 Halo/current ratios
46 NMR <125>, 125 pk, CW
47 NMR <125>, 188 pk, df 2/3
48 NMR < 83>, 125 pk, df 2/3
49 NMR <250>, 250 pk, CW
50 NMR < 83>, 250 pk, df 1/3
51 NMR <167>, 250 pk, df 2/3
52 NMR <333>, 500 pk, df 2/3
53 NMR <500>, 750 pk, df 2/3
54 NMR <750>, 750 pk, CW
55 NMR < 50>, 750 pk, df 1/15
56 - the end -
